ANEXA 4
GRAFIC GANTT

LUCRARI REPARATII HIDROIZOLATII TERASA SCJUPB, CORP F - BLOC OPERATOR

SPITALUL CLINIC JUDETEAN DE URGENTA “PIUS BRÎNZEU” TIMISOARA

Întocmit,

Nr. 004/1260/2023

ID		Task Mode	Task Name	Duration	Start	Finish
1			**LUCRARI DE REPARATIE HIDROIZOLATIE TERASA CORP F SCJUPBT - BLOC OPERATOR**	**43 days**	**Fri 9/1/23**	**Tue 10/31/23**
2			Ordin de incepere	0 days	Fri 9/1/23	Fri 9/1/23
3			Perioada mobilizare si organizare de santier	5 days	Fri 9/1/23	Thu 9/7/23
4			Desfaceri guri de scurgere si aerisiri termoizolatii	2 days	Fri 9/8/23	Mon 9/11/23
5			Desfaceri tabla atic	2 days	Tue 9/12/23	Wed 9/13/23
6			Curatarea terasei prin indepartarea stratului de ardezie existent	3 days	Thu 9/14/23	Mon 9/18/23
7			Montaj guri de scurgere si aerisiri inclusiv refacere straturi sistem termo-hidroizolant	5 days	Tue 9/19/23	Mon 9/25/23
8			Montaj membrana bituminoasa terasa prin liprire cu flacara	15 days	Tue 9/26/23	Mon 10/16/23
9			Montaj profile metalice sigilare rost la imbinarea cu peretele	3 days	Tue 10/17/23	Thu 10/19/23
10			Montaj tabla atic recuperata	5 days	Fri 10/20/23	Thu 10/26/23
11			Curatenie	3 days	Fri 10/27/23	Tue 10/31/23
12			Receptia la terminarea lucrarilor	0 days	Tue 10/31/23	Tue 10/31/23

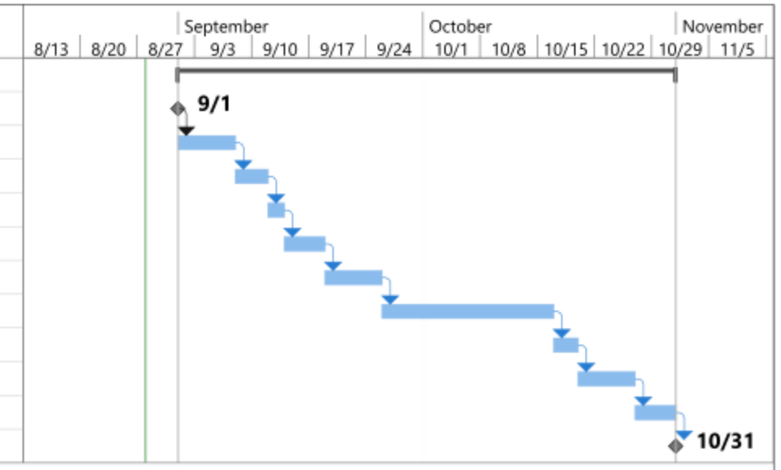

Project: Project hidroizolatii ter
Date: Mon 8/28/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
